

## UCAMA Construction Report #11

Because of the number of inquiries we have received regarding the progress of our new museum facility on Jasper Avenue, UCAMA has decided to prepare month end construction reports. These reports will be sent out to our friends and supporters until Phase 1 is complete.



June has been a particularly productive month on the construction site. The last of the concrete pillars have been poured. It is particularly gratifying to stand on the main floor and look down the row of slanted, oblique pillars reach gracefully to the sky.

The steel girders are firmly nestled into place on the top of the western wall.




The upper gallery deck facing Jasper Avenue has been poured and for the first time since demolition was completed it's possible to appreciate our magnificent view of the Saskatchewan River valley.





Inside our new home, walls are being erected in the basement and pipes are being hung.

If all this were not enough, on June 15 we filmed a video on site in support of our new Kickstarter fundraising campaign. You can view this video on our [Kickstarter page](#) to get a close up look at the progression of the building.

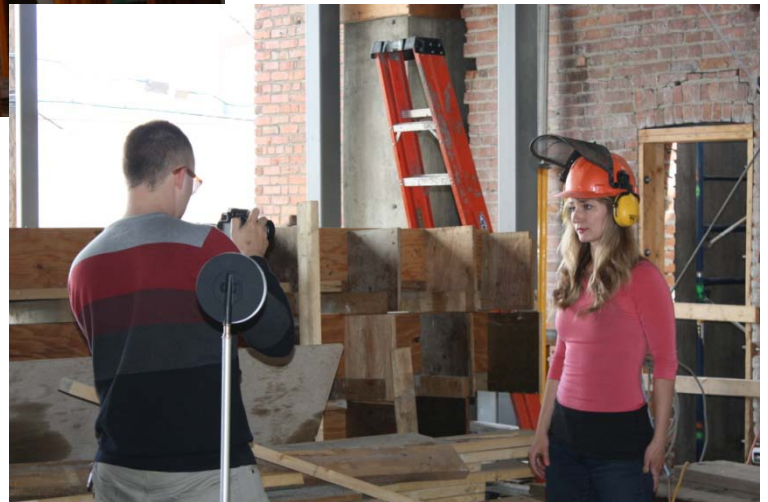

Looking to the future, on July 15 the crane will be removed from the elevator shaft. This is a monumental date signaling that the major steel girders are in place and the concrete is poured. Work on the roof is scheduled to commence on August 1. Aluminum cladding is scheduled to be on the site in 60 days.

Stay tuned for further updates next month.

June 30, 2014
